ID	Task Name	Duration	Start	Finish
1	3 Wk Look ahead LOSOS	15 days	Mon 3/26/12	Fri 4/13/12
2	3-26-2012 to 4-13-2012	15 days	Mon 3/26/12	Fri 4/13/12
3	Plumbing rough Continuous	15 days	Mon 3/26/12	Fri 4/13/12
4	HVAC rough Continuous	15 days	Mon 3/26/12	Fri 4/13/12
5	Fan boxes 1st floor	7 days	Mon 3/26/12	Tue 4/3/12
6	Fan box MEP Rough	10 days	Mon 3/26/12	Fri 4/6/12
7	Cabinet unit heaters hang	10 days	Mon 3/26/12	Fri 4/6/12
8	Elec rough Continuous	15 days	Mon 3/26/12	Fri 4/13/12
9	Permanent temp power turn over	5 days	Mon 3/26/12	Fri 3/30/12
10	Sprinkler rough	15 days	Mon 3/26/12	Fri 4/13/12
11	Roofing detailing and penetrations at Curb	5 days	Mon 3/26/12	Fri 3/30/12
12	Exterior wall insul	5 days	Mon 3/26/12	Fri 3/30/12
13	Exterior wall wood furring	5 days	Mon 3/26/12	Fri 3/30/12
14	Curtain wall framing CW 3 and 4	5 days	Mon 4/2/12	Fri 4/6/12
15	Curtain wall glazing CW3 and 4	5 days	Mon 4/2/12	Fri 4/6/12
16	ACM panels at windows	5 days	Mon 3/26/12	Fri 3/30/12
17	Wood Siding	15 days	Mon 3/26/12	Fri 4/13/12
18	Metal panel penthouse/ stairs	10 days	Mon 3/26/12	Fri 4/6/12
19	1st floor rough inspections	1 day	Mon 3/26/12	Mon 3/26/12
20	Hibay and PH. rough inspection	5 days	Mon 3/26/12	Fri 3/30/12
21	Wall taping and sanding 2nd floor	5 days	Mon 3/26/12	Fri 3/30/12
22	Sheet rock 1st floor Continuous	15 days	Mon 3/26/12	Fri 4/13/12
23	Ceramic tile	10 days	Mon 4/2/12	Fri 4/13/12
24	Prime paint	13 days	Wed 3/28/12	Fri 4/13/12
25	Mono rail install modification	4 days	Tue 3/27/12	Fri 3/30/12
26	Bridge crane	1 day	Tue 3/27/12	Tue 3/27/12
27	Elevator install	14 days	Tue 3/27/12	Fri 4/13/12
28	Sheetrock PH.	5 days	Mon 4/2/12	Fri 4/6/12

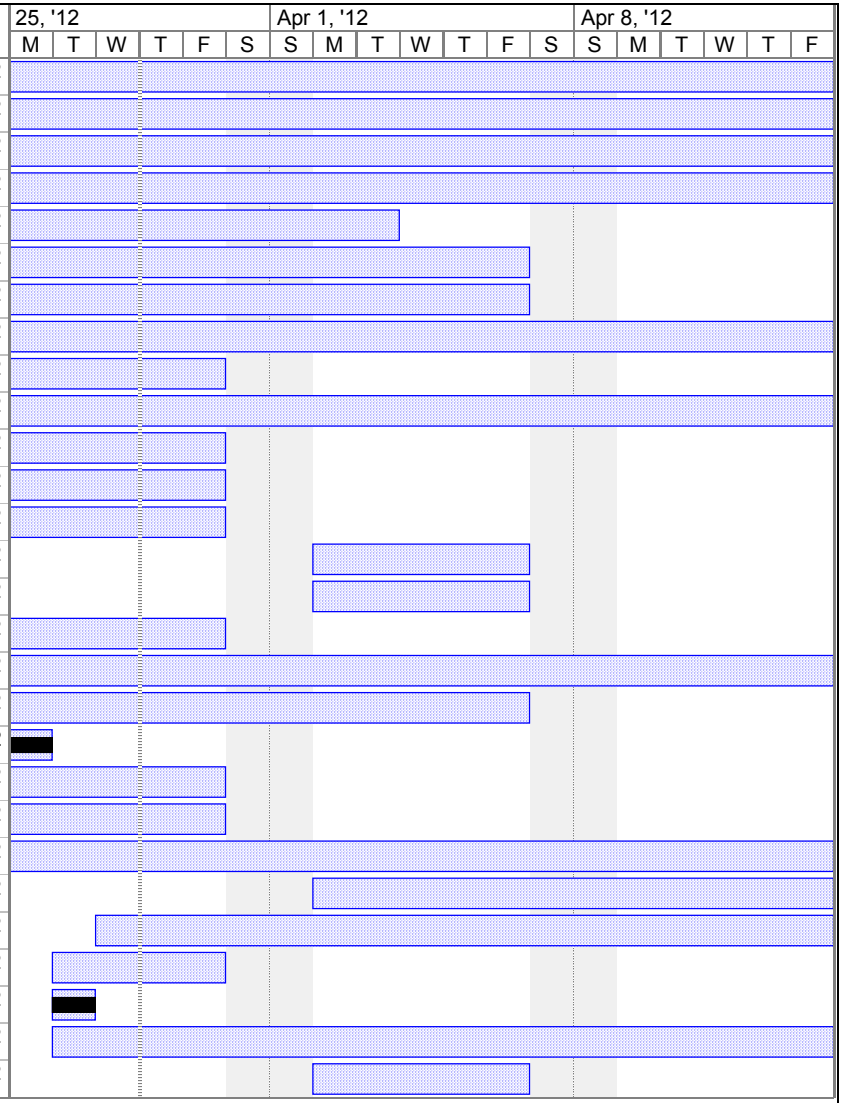

Project: 3 week look ahead 3-26- 201
Date: Thu 3/29/12

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
